


# SEMSWA CIP Project Status Update

July 2011

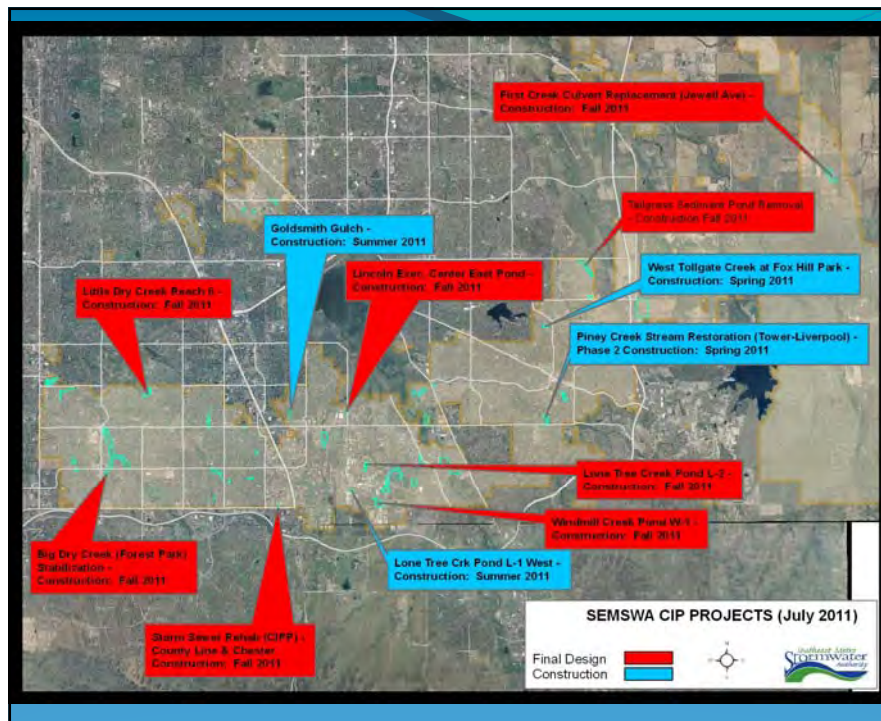

## PROJECT: Piney Creek Stabilization (Tower to Liverpool)

DESCRIPTION: Design and construction of stream stabilization of Piney Creek

BUDGET: \$550,000

STATUS: Completed

CHANGE SINCE LAST REPORT:  
**CONSTRUCTION COMPLETE**

MILESTONES:

**Construction Completion  
June 2011**



## PROJECT: PINEY CREEK (TOWER TO LIVERPOOL)



PROJECT: PINEY CREEK (TOWER TO LIVERPOOL)



PROJECT: West Toll Gate Creek at Foxhill Park

DESCRIPTION: **Design and construction of stream stabilization improvements**


BUDGET: **\$350,000**

STATUS: **COMPLETED**

CHANGE SINCE LAST REPORT:  
**CONSTRUCTION COMPLETE**

MILESTONES:

**Construction Completion  
June 2011**

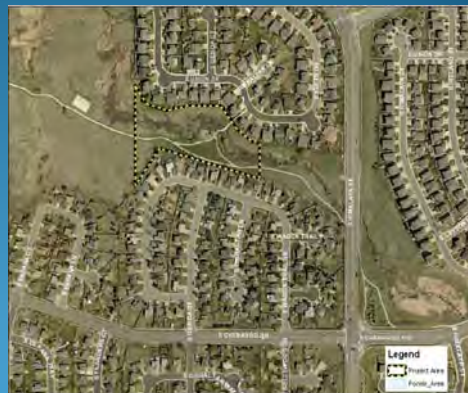



PROJECT: West Toll Gate Cr. at Foxhill Park



PROJECT: West Toll Gate Cr. at Foxhill Park



## PROJECT: West Toll Gate Cr. at Foxhill Park



## PROJECT: Lone Tree Creek Pond L-1 West

**DESCRIPTION:** Design and construction of the regional stormwater pond.

**BUDGET:** \$225,000

**STATUS:** CONSTRUCTION COMPLETED

**CHANGE SINCE LAST REPORT:**

**Construction Completed**

**MILESTONES:**

**Construction Completion  
June 2011**



PROJECT: POND L1 WEST



PROJECT: POND L1 WEST





## PROJECT: POND L1 WEST



## PROJECT: GOLDSMITH GULCH (PHASE 1) – CALEY CULVERT REPLACEMENT

**DESCRIPTION:** Design and construction of new culvert at Caley Avenue.

**BUDGET:** \$265,000


**STATUS:** CONSTRUCTION  
**STARTED JUNE 13, 2011**

**CHANGE SINCE LAST REPORT:**

**Construction Started**

**MILESTONES:**

**Construction Completion**  
**August 2011**

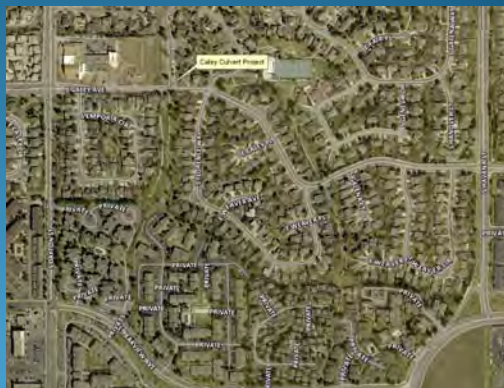

## PROJECT: GOLDSMITH GULCH



## PROJECT: GOLDSMITH GULCH (PHASE 1)





## PROJECT: GOLDSMITH GULCH (PHASE 1)



### DESIGN PROJECTS ( FALL 2011 CONSTRUCTION START)

<u>PROJECT</u>	<u>TOTAL ESTIMATED COST (\$)</u>	<u>SEMSWA ESTIMATED COST (\$)</u>
JEWELL AVENUE CULVERT REPLACEMENT	250,000	250,000
LINCOLN EXECUTIVE CENTER EAST POND	390,000	390,000
WINDMILL CREEK POND W-1 (PHASE 1)	850,000	850,000
FOREST PARK - TRIBUTARY B STABILIZATION	280,000	280,000
LONE TREE CREEK POND L-2 (PHASE 1)	560,000	560,000
TALLGRASS SEDIMENT POND REMOVAL	285,000	285,000
DOVE CREEK POND D-2	750,000	750,000
COUNTY LINE & CHESTER CULVERT CIPP	150,000	150,000
LITTLE DRY CREEK REACH 6 STABILIZATION	650,000	650,000
TOTAL	4,165,000	4,165,000
