


# SEMSWA CIP Project Status Update

April 2012

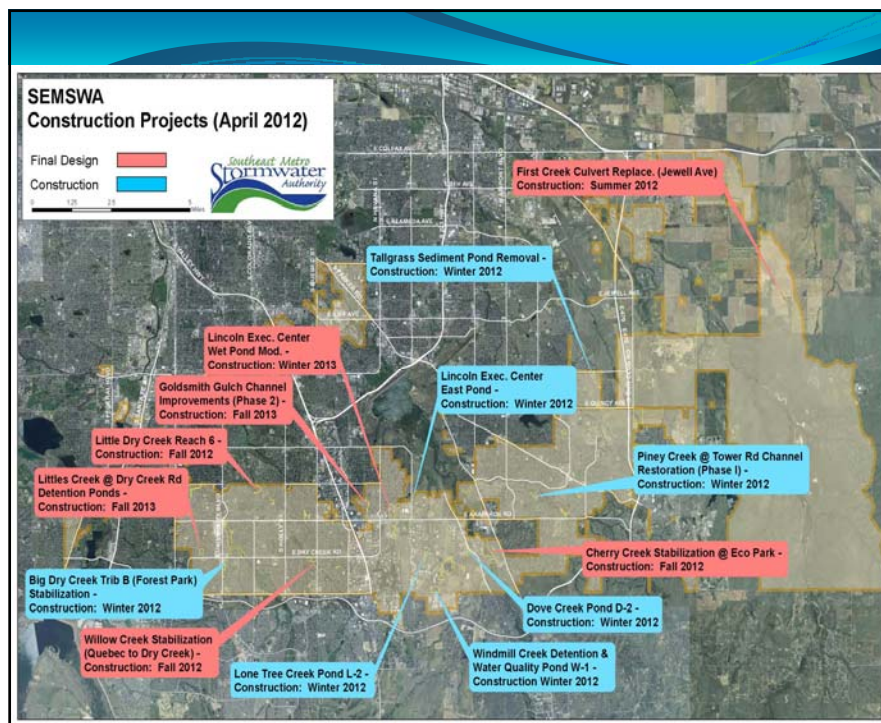

## PROJECT: DOVE CREEK REGIONAL POND D-2

### DESCRIPTION:

CONSTRUCTION OF REGIONAL  
DETENTION -WATER QUALITY  
POND

BUDGET: \$803,380

STATUS: CONSTRUCTION IN  
PROGRESS

CHANGE SINCE LAST REPORT:  
75% Complete

### MILESTONES:

Construction Complete:  
June 2012



## PROJECT: DOVE CREEK REGIONAL POND D-2



## PROJECT: WINDMILL CREEK REGIONAL POND W-1

DESCRIPTION:  
CONSTRUCTION OF REGIONAL  
DETENTION -WATER QUALITY  
POND

BUDGET: \$916,715

STATUS: CONSTRUCTION  
STARTED

CHANGE SINCE LAST REPORT:  
30% Complete

MILESTONES:  
Construction Complete:  
June 2012



## PROJECT: WINDMILL CREEK REGIONAL POND W-1



## PROJECT: LONE TREE CREEK REGIONAL POND L-2

### DESCRIPTION:

CONSTRUCTION OF REGIONAL  
DETENTION POND

BUDGET: \$686,483

STATUS: CONSTRUCTION IN  
PROGRESS

CHANGE SINCE LAST REPORT:  
15% Complete

### MILESTONES:

Construction Complete:  
July 2012



## PROJECT: LINCOLN EXECUTIVE CENTER EAST POND

### DESCRIPTION:

CONSTRUCTION OF SUB-  
REGIONAL DETENTION  
& WATER QUALITY POND

BUDGET: \$366,530

STATUS: CONSTRUCTION  
COMPLETED

CHANGE SINCE LAST REPORT:  
100% Complete

### MILESTONES:

Construction Complete:  
March 2012





## PROJECT: LINCOLN EXECUTIVE CENTER EAST POND



## PROJECT: BIG DRY CREEK TRIBUTARY B – CHANNEL IMPROVEMENTS

### DESCRIPTION:

CONSTRUCTION OF 950'  
CHANNEL IMPROVEMENTS

BUDGET: \$267,330

STATUS: CONSTRUCTION IN  
PROGRESS

CHANGE SINCE LAST REPORT:  
75% Complete

### MILESTONES:

Construction Complete:  
May 2012



## PROJECT: BIG DRY CREEK TRIBUTARY B – CHANNEL IMPROVEMENTS



## PROJECT: TALLGRASS SEDIMENT POND REMOVAL

DESCRIPTION: REMOVAL OF  
TWO SEDIMENT BASINS


BUDGET: \$255,725

STATUS: CONSTRUCTION IN  
PROGRESS

CHANGE SINCE LAST REPORT:  
Construction Started

MILESTONES:

Construction Complete:  
June 2012

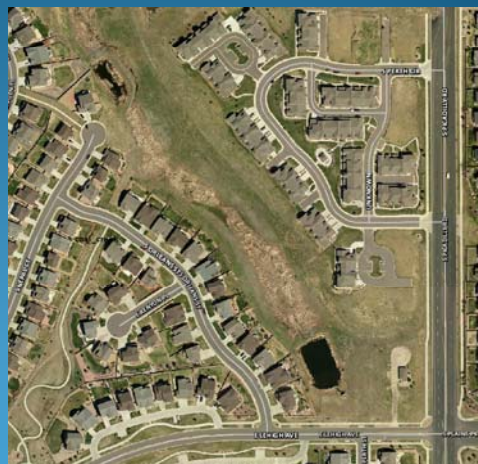

FALL - WINTER 2011/2012 CONSTRUCTION PROJECTS			
<u>PROJECT</u>	<u>ESTIMATED COST (\$)</u>	<u>ESTIMATED COST for PROJECTS BID (\$)</u>	<u>LOW BID (\$)</u>
JEWELL AVENUE CULVERT REPLACEMENT	320,000		
LINCOLN EXECUTIVE CENTER EAST POND	390,000	390,000	366,530
WINDMILL CREEK POND W-1 (PHASE 1)	850,000	850,000	763,764
FOREST PARK - TRIBUTARY B STABILIZATION	280,000	280,000	232,461
LONE TREE CREEK POND L-2 (PHASE 1)	700,000	700,000	588,712
TALLGRASS SEDIMENT POND REMOVAL	285,000	285,000	255,725
DOVE CREEK POND D-2	750,000	750,000	647,073
<b>TOTAL</b>	<b>3,575,000</b>	<b>3,255,000</b>	<b>2,854,265 (88%)</b>
